

Peak Apparels Ltd.

Vogra, National University, Joydevpur, Gazipur, Dhaka

(23.970027N, 90.381149E)


29 June 2014



Observations



Peak Apparels was under construction at the time of survey. The RC frame had been constructed up to 4th floor slab.

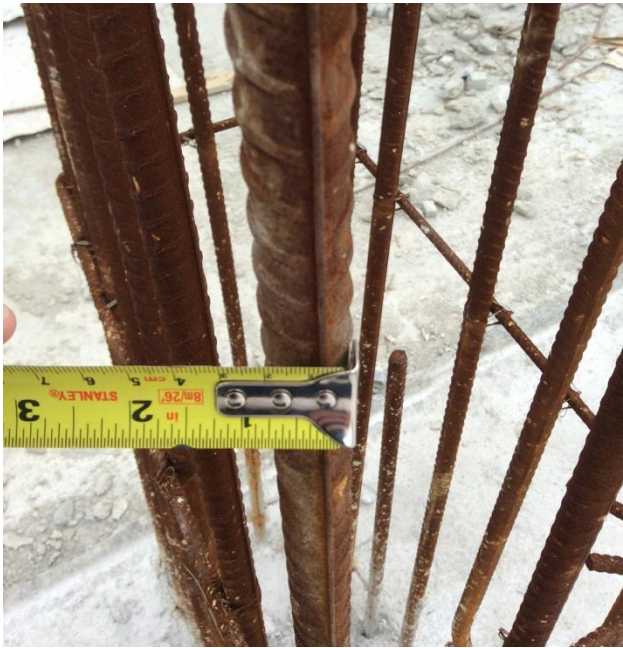

High strength rebar was observed in the column reinforcement at 4rd floor





Lower floor concrete surfaces had already been plastered and finished



Areas of the 3rd floor slab were still propped and had recently been cast



Eccentric beams were observed – the Project Engineer advised that eccentricities had been accounted for in column design



50mm screed and tiles measured

Building activities included installation of floor finishes and internal wall construction

