



Aboni Knitwear (New Shed)

169-171, 195-196, Tatulzhora, Hemayetpur, Savar, Dhaka

(23.792721N, 90.26075E)

3rd February 2019





Observation



Inconsistency in roof bracing system




Inconsistency observed in roof bracing system. Building engineer is required to review the existing bracing system for the lateral stability.

Observation



Presence of gaps in remedial works

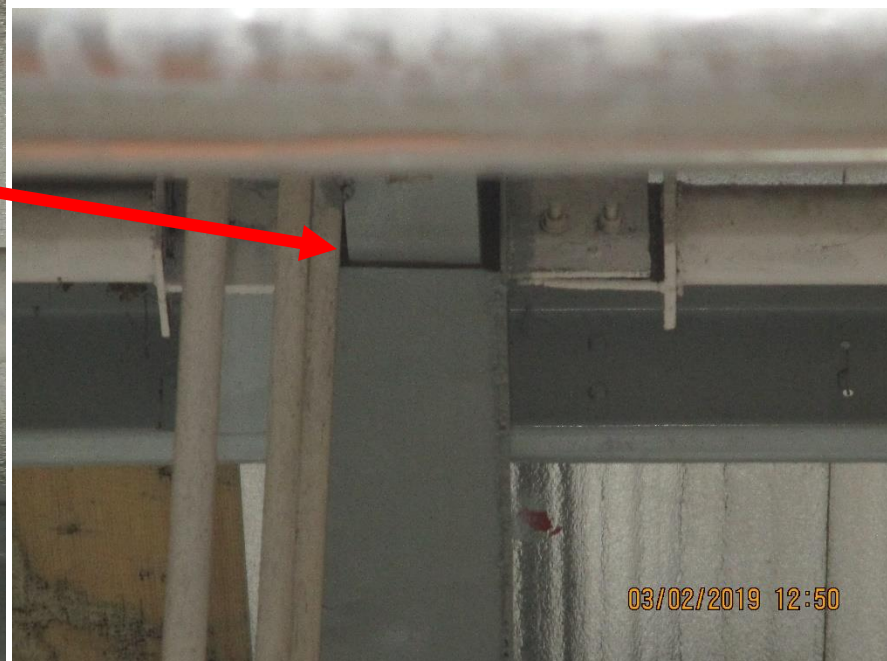

Significant gap between retrofitted column & rafter were observed in several locations. Building engineer is required to carry out remedial works.

Observation



Priority Action



Problem Observed

- 1: Inconsistency in roof bracing system.
- 2: Presence of gaps in remedial works.



Item No.	Observation	Recommended Action Plan	Recommended Timeline
1	Inconsistency in roof bracing system	Building engineer is required to review the existing bracing system for the lateral stability.	6-weeks
2	Inconsistency in roof bracing system	Carryout any remedial actions suggested by factory engineer.	6-months
3	Presence of gaps in remedial works	Factory engineer is required to carry out the remediation work of the connections.	6-weeks
